Immanuel Road
Construction Schedule

ID	Task Name	Duration	Start	Finish
1	**Utility Relocations**	282 days	Thu 6/26/25	Tue 8/25/26
2	**Immanuel Road**	**479 days**	**Tue 9/8/26**	**Thu 7/27/28**
3	**Notice To Proceed**	0 days	Tue 9/8/26	Tue 9/8/26
4	MILESTONE #1 (One Way Traffic)	85 days	Wed 9/23/26	Mon 2/8/27
5	MILESONE #2 (One Way Traffic)	19 days	Mon 1/25/27	Thu 2/18/27
6	MILESTONE #3 (One Way Traffic)	232 days	Fri 9/18/26	Fri 9/24/27
7	**Phase 1**	**30 days**	**Tue 9/8/26**	**Mon 10/19/26**
8	Truss Bridge Deck Removal and Cleanup	20 days	Tue 9/8/26	Mon 10/5/26
9	Truss Bridge Lifting, Removal, Cleanup, and Relocation	10 days	Tue 10/6/26	Mon 10/19/26
10	**Phase 1 Step 1**	**171 days**	**Tue 9/29/26**	**Mon 6/14/27**
11	Initial Traffic Control	1 day	Wed 9/30/26	Wed 9/30/26
12	Erosion Control Devices (Phase 1)	2 days	Tue 9/29/26	Wed 9/30/26
13	Prep ROW	4 days	Thu 10/1/26	Tue 10/6/26
14	Eliminate Existing Pavement Markings	1 day	Thu 10/1/26	Thu 10/1/26
15	Workzone Pavement Markings	2 days	Thu 10/1/26	Fri 10/2/26
16	Install Positive Barrier (LPCB)	4 days	Fri 10/2/26	Wed 10/7/26
17	Construct Killingsworth Lane Repair	2 days	Thu 10/1/26	Fri 10/2/26
18	Initiate Phase 1 Traffic Shift	1 day	Mon 10/5/26	Mon 10/5/26
19	Excavation	20 days	Tue 10/6/26	Mon 11/2/26
20	Embankment	20 days	Tue 10/6/26	Mon 11/2/26
21	Temporary Retaining Walls/Shoring	15 days	Tue 10/27/26	Mon 11/16/26
22	Retaining Walls (MSE Walls)	45 days	Tue 10/27/26	Fri 1/15/27
23	Storm Sewer Pipe	60 days	Tue 10/20/26	Fri 1/29/27
24	Inlets & Manholes	75 days	Tue 11/17/26	Fri 3/19/27
25	Lime Treat Subgrade	20 days	Wed 3/10/27	Tue 4/6/27
26	Lime Treat Cure Time	5 days	Wed 4/7/27	Tue 4/13/27
27	Flex Base Material	11 days	Wed 4/14/27	Wed 4/28/27
28	Flex Base Cure Time	3 days	Thu 4/29/27	Mon 5/3/27
29	Prime Coat	1 day	Tue 5/4/27	Tue 5/4/27
30	Hox Mix Asphalt (Base)	10 days	Wed 5/5/27	Tue 5/18/27
31	Constructing Detours (Temp Pave)	9 days	Wed 5/19/27	Mon 5/31/27
32	Temporary Signals	10 days	Tue 6/1/27	Mon 6/14/27
33	**Gilleland Creek Bridge**	**55 days**	**Tue 10/20/26**	**Fri 1/22/27**
34	Drilled Shafts	4 days	Tue 10/20/26	Fri 10/23/26
35	Concrete Abutment	7 days	Wed 10/28/26	Thu 11/5/26
36	Concrete Bent (Multi-Column)	12 days	Mon 11/2/26	Tue 11/17/26
37	Concrete Curing	7 days	Wed 11/18/26	Wed 12/2/26
38	Concrete Beams (Simple Span) Span 1	1 day	Thu 12/3/26	Thu 12/3/26
39	Concrete Beams (Simple Span) Span 2	1 day	Fri 12/4/26	Fri 12/4/26
40	Concrete Beams (Simple Span) Span 3	1 day	Mon 12/7/26	Mon 12/7/26
41	Bridge Decks	6 days	Fri 12/4/26	Fri 12/11/26
42	Deck curing	20 days	Mon 12/14/26	Fri 1/22/27
43	**Gilleland Creek Tributary No. 2 Bridge**	**83 days**	**Fri 10/30/26**	**Mon 3/15/27**
44	Drilled Shafts	2 days	Fri 10/30/26	Mon 11/2/26
45	Concrete Abutment	7 days	Thu 11/5/26	Fri 11/13/26
46	Concrete Bent (Multi-Column)	14 days	Tue 11/10/26	Wed 1/27/27
47	Concrete Curing	7 days	Thu 1/28/27	Fri 2/5/27
48	Concrete Beams (Simple Span) Span 1	1 day	Mon 2/8/27	Mon 2/8/27
49	Concrete Beams (Simple Span) Span 2	1 day	Tue 2/9/27	Tue 2/9/27
50	Bridge Decks	4 days	Wed 2/10/27	Mon 2/15/27
51	Deck Curing	20 days	Tue 2/16/27	Mon 3/15/27
52	**Phase 1 Step 2 (Gilleland Creek)**	**5 days**	**Mon 1/25/27**	**Fri 1/29/27**
53	TCP - Immanuel Road Closure	1 day	Mon 1/25/27	Mon 1/25/27
54	Temporary Retaining Walls	2 days	Tue 1/26/27	Wed 1/27/27
55	Construct Perm Pavement	3 days	Tue 1/26/27	Thu 1/28/27
56	Construct Detour	1 day	Thu 1/28/27	Thu 1/28/27
57	install TCP Devices (LPCTB)	1 day	Fri 1/29/27	Fri 1/29/27
58	**Phase 2**	**152 days**	**Tue 6/15/27**	**Wed 1/12/28**

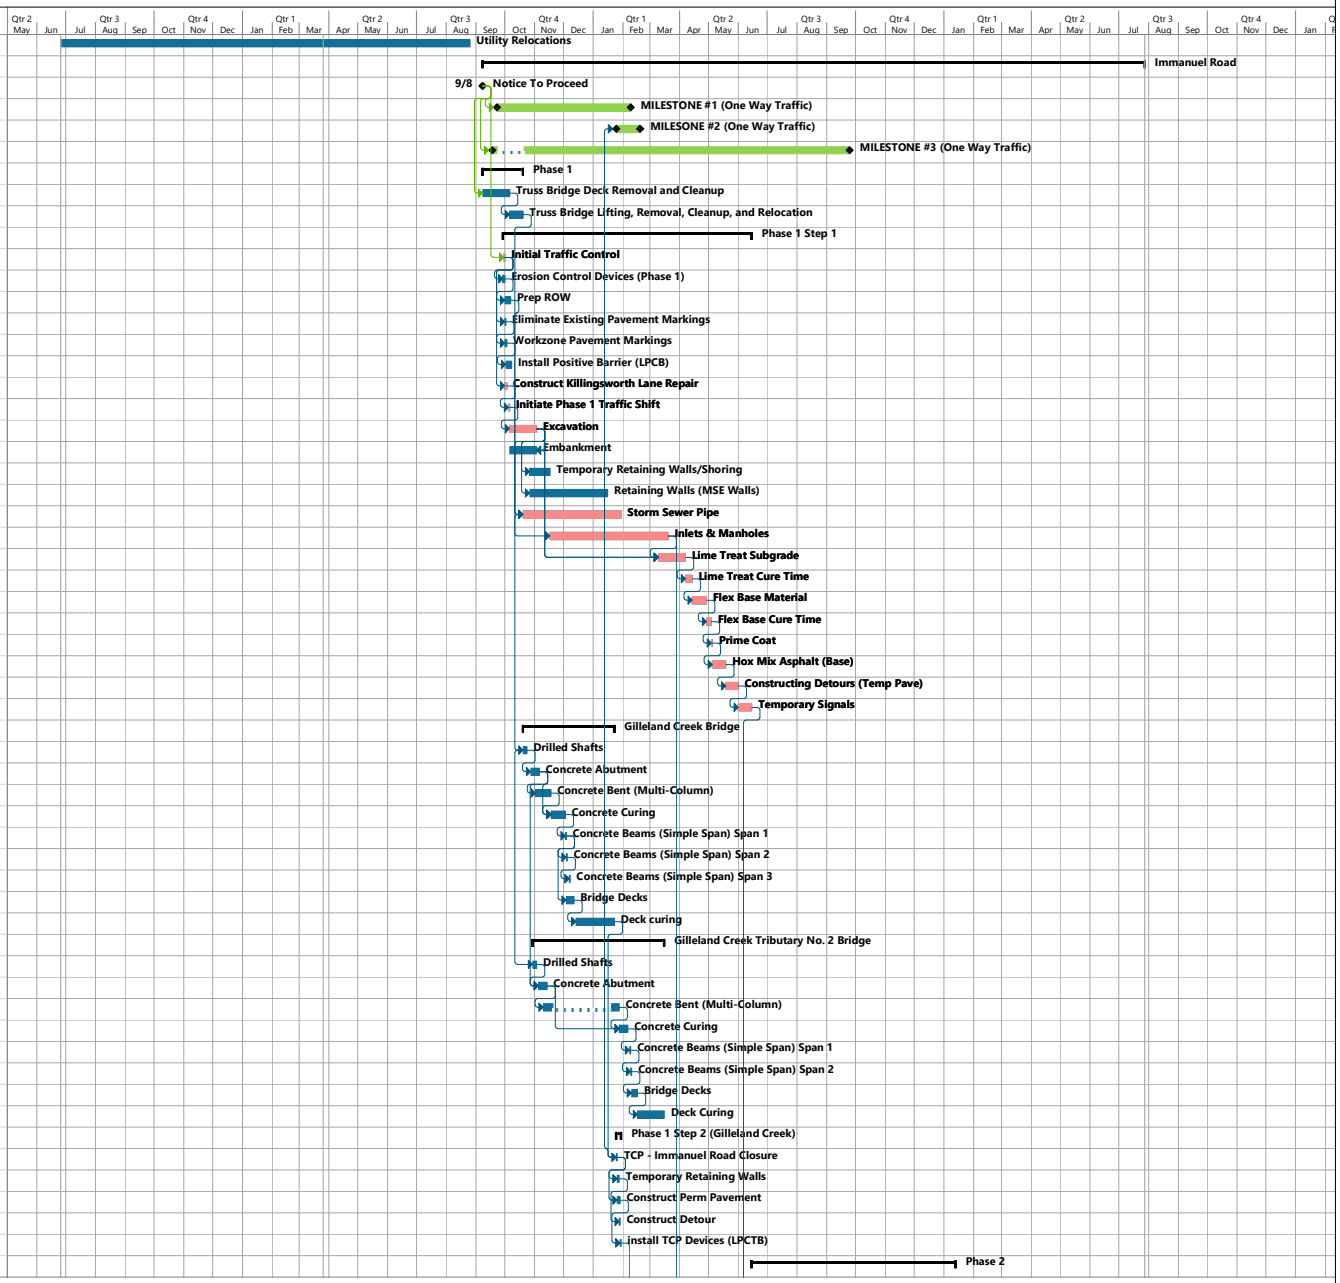

Rodriguez Transportion Group, Inc.
Immanuel Road
Date: Thu 3/26/26

Critical Split · · · · · · · · · · · · Task ▬▬▬ Milestone ◆ Summary ◆▬▬◆ Critical ▬▬▬

Immanuel Road
Construction Schedule

ID	Task Name	Duration	Start	Finish
59	Initial Traffic Control	1 day	Tue 6/15/27	Tue 6/15/27
60	Erosion Control Devices (Phase 2)	2 days	Tue 6/15/27	Wed 6/16/27
61	Eliminate Existing Pavement Markings	1 day	Wed 6/16/27	Wed 6/16/27
62	Workzone Pavement Markings	2 days	Wed 6/16/27	Thu 6/17/27
63	Move Positive Barrier (LPCB)	2 days	Fri 6/18/27	Mon 6/21/27
64	Initiate Phase 2 Traffic Shift	1 day	Tue 6/22/27	Tue 6/22/27
65	Excavation	20 days	Wed 6/23/27	Tue 7/20/27
66	Embankment	20 days	Wed 6/23/27	Tue 7/20/27
67	Retaining Walls (MSE Walls)	40 days	Wed 7/21/27	Tue 9/14/27
68	Rail/MBGF	1 day	Tue 9/14/27	Tue 9/14/27
69	Storm Sewer Pipe	15 days	Wed 7/21/27	Tue 8/10/27
70	Inlets & Manholes	60 days	Wed 8/4/27	Tue 10/26/27
71	Lime Treat Subgrade	20 days	Wed 10/20/27	Tue 11/16/27
72	Lime Treat Cure Time	5 days	Wed 11/17/27	Tue 11/23/27
73	Flex Base Material	9 days	Wed 11/24/27	Mon 12/6/27
74	Flex Base Cure Time	3 days	Tue 12/7/27	Thu 12/9/27
75	Prime Coat	1 day	Fri 12/10/27	Fri 12/10/27
76	Hot Mix Asphalt (Base)	7 days	Mon 12/13/27	Tue 12/21/27
77	Concrete Curb & Gutter	16 days	Wed 12/22/27	Wed 1/12/28
78	**Gilleland Creek Bridge**	**39 days**	**Wed 8/11/27**	**Mon 10/4/27**
79	Drilled Shafts	4 days	Wed 8/11/27	Mon 8/16/27
80	Concrete Abutment	7 days	Tue 8/17/27	Wed 8/25/27
81	Concrete Bent (Multi-Column)	12 days	Thu 8/26/27	Fri 9/10/27
82	Concrete Curing	7 days	Mon 9/13/27	Tue 9/21/27
83	Concrete Beams (Simple Span) Span 1	1 day	Wed 9/22/27	Wed 9/22/27
84	Concrete Beams (Simple Span) Span 2	1 day	Thu 9/23/27	Thu 9/23/27
85	Concrete Beams (Simple Span) Span 3	1 day	Fri 9/24/27	Fri 9/24/27
86	Bridge Decks	4 days	Fri 9/24/27	Wed 9/29/27
87	Bridge Rails	3 days	Thu 9/30/27	Mon 10/4/27
88	**Gilleland Creek Tributary No. 2 Bridge**	**31 days**	**Mon 8/23/27**	**Mon 10/4/27**
89	Drilled Shafts	2 days	Mon 8/23/27	Tue 8/24/27
90	Concrete Abutment	7 days	Wed 8/25/27	Thu 9/2/27
91	Concrete Bent (Multi-Column)	6 days	Fri 9/3/27	Fri 9/10/27
92	Concrete Curing	7 days	Mon 9/13/27	Tue 9/21/27
93	Concrete Beams (Simple Span) Span 1	1 day	Wed 9/22/27	Wed 9/22/27
94	Concrete Beams (Simple Span) Span 2	1 day	Thu 9/23/27	Thu 9/23/27
95	Bridge Decks	4 days	Fri 9/24/27	Wed 9/29/27
96	Bridge Rails	3 days	Thu 9/30/27	Mon 10/4/27
97	**Phase 3**	**130 days**	**Thu 1/13/28**	**Wed 7/12/28**
98	Initial Traffic Control	1 day	Thu 1/13/28	Thu 1/13/28
99	Remove Positive Barrier (LPCB)	2 days	Fri 1/14/28	Mon 1/17/28
100	Eliminate Existing Pavement Markings	1 day	Tue 1/18/28	Tue 1/18/28
101	Workzone Pavement Markings	2 days	Wed 1/19/28	Thu 1/20/28
102	Initiate Traffic Shift	1 day	Fri 1/21/28	Fri 1/21/28
103	Remove Temporary Pavement	3 days	Mon 1/24/28	Wed 1/26/28
104	Storm Sewer Pipe	2 days	Thu 1/27/28	Fri 1/28/28
105	Inlets & Manholes	60 days	Mon 1/31/28	Fri 4/21/28
106	Hot Mix Asphalt (Base)	1 day	Thu 1/27/28	Thu 1/27/28
107	Curb & Gutter	16 days	Fri 4/14/28	Fri 5/5/28
108	Sidewalk	35 days	Fri 4/28/28	Thu 6/15/28
109	Permanent Signals	20 days	Fri 5/19/28	Thu 6/15/28
110	Illumination Poles/Conduit	7 days	Fri 6/16/28	Mon 6/26/28
111	Permanent Small Signs	4 days	Wed 6/21/28	Mon 6/26/28
112	Seeding & Landscape	12 days	Tue 6/27/28	Wed 7/12/28
113	**Phase 4**	**11 days**	**Thu 7/13/28**	**Thu 7/27/28**
114	Hot Mix Asphalt (Final Course)	6 days	Thu 7/13/28	Thu 7/20/28
115	Final Striping	3 days	Fri 7/21/28	Tue 7/25/28
116	Final Clean Up	2 days	Wed 7/26/28	Thu 7/27/28

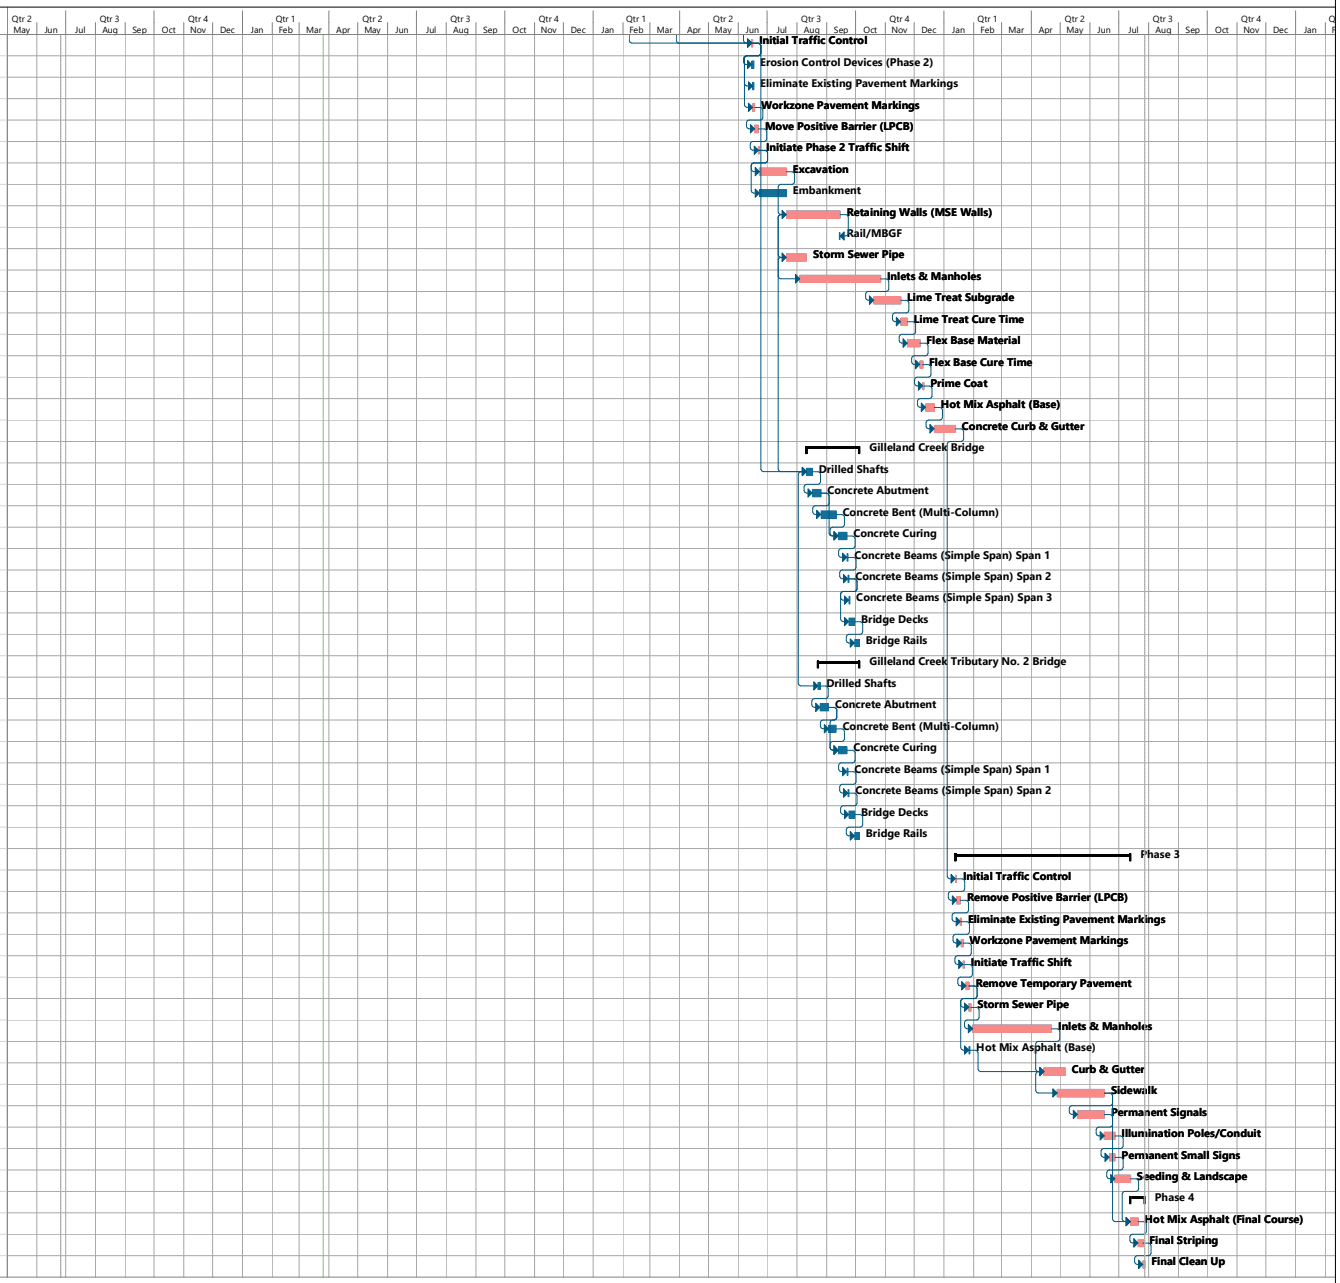

Rodriguez Transportion Group, Inc.
Immanuel Road
Date: Thu 3/26/26

Critical Split · · · · · · · · · · · · Task — Milestone ◆ Summary — Critical
